



No TET 73/GWT/2006

March 28, 2006

To
Mr. V.C. Elias
Managing Partner
United Construction Company
VMC Complex, Wadakkanchery
Thrissur - 680 590.

Dear sir,

**Sub: Construction of surface water tank, Jyothi Engineering College,
Cheruthuruthy - Work awarding of**

Ref: Your offer for the work

With reference to your offer cited above and subsequent personal discussion we had with you, the Trust is happy to award the work to you at the rate of 20% (Twenty percentage) above the estimate rate of Rs. 3,73,335/- (Rupees Three Lakh Seventy Three Thousand Three Hundred and Thirty Five Only), the rate offered by you on negotiation. The work is awarded subject to the following conditions

1. The rate includes all sorts of lead and lift required for the work and transport of materials to site
2. The existing water supply and electrical supply extended to your construction site can be utilized. The contractor has to meet the recurring expenditure towards electricity charges and maintenance, if any found required.
3. The general and special conditions of contract already in force are applicable to this work also.
4. You are requested to execute an agreement in Kerala Govt. Stamp paper worth Rs.50/- after depositing an amount of Rs.25,000/- towards security deposit.

True Copy Attested

Thomas Mathew

Yours faithfully,

Thomas Mathew

Thomas Mathew
Jl. Secretary

C.O. to the Project Manager
Dr. SUNNY JOSEPH KALAYATHANKAL Project Engineer
M.Tech, MCA, M.Sc, M.Phil, B.Ed
Ph.D (Computer Science), Ph.D (Maths) Finance Manager
PRINCIPAL
Jyothi Engineering College
Cheruthuruthy P.O. - 679 531




CREATING TECHNOLOGY
LEADERS OF TOMORROW
ESTD 2002

NBA accredited B.Tech Programmes in Computer Science & Engineering, Electronics & Communication Engineering, Electrical & Electronics Engineering and Mechanical Engineering valid for the academic years 2016-2022. NBA accredited B.Tech Programme in Civil Engineering valid for the academic years 2019-2022.

7.1.4 Water conservation facilities available in the Institution

Construction of tanks- Details of Water Tank of 30 Lakh capacity

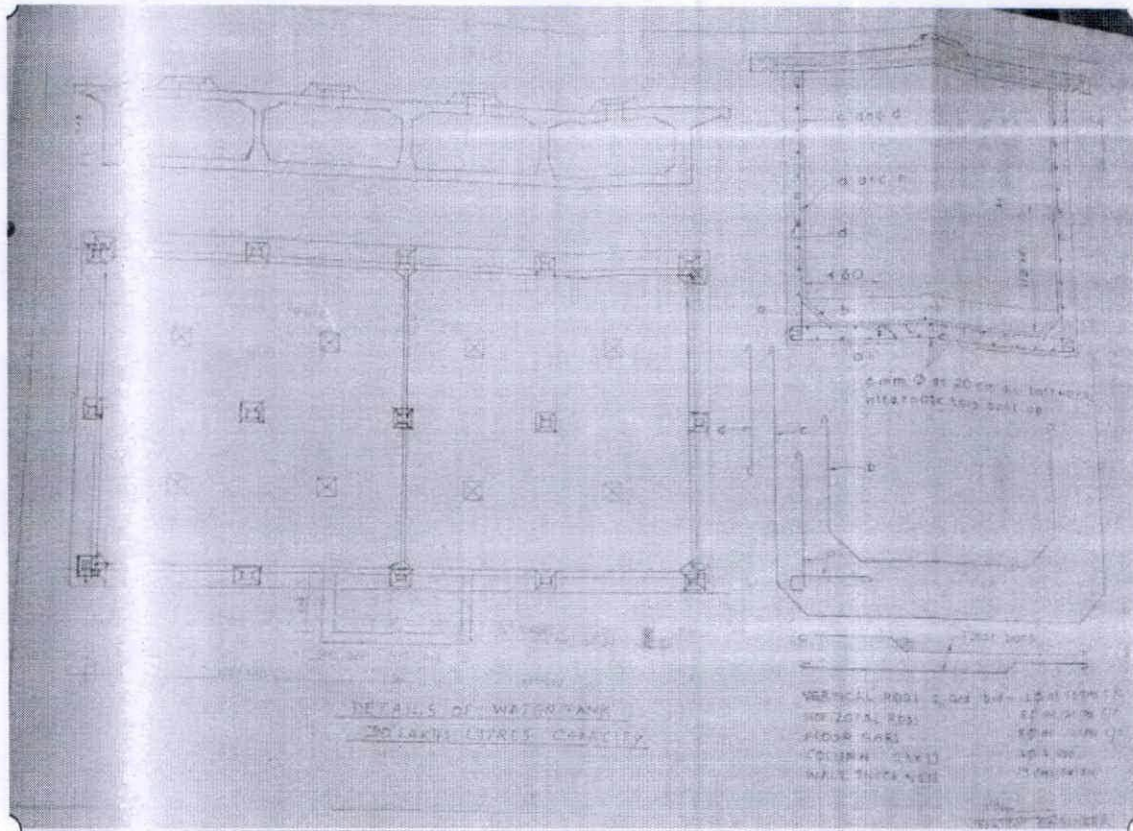

Dr. SUNNY JOSEPH KALAYATHANKAL
 M.Tech, MCA, M.Sc, M.Phil, B.Ed
 Ph.D (Computer Science), Ph.D (Maths)
 PRINCIPAL
 Jyothi Engineering College
 Cheruthuruthy P.O.- 679 531

Amud

True Copy Attested

Construction of Surface water tank - Jyothi Engineering College,

C.C.1st & Final

Item No	Particulars	Agd. Qty	Up to date Qty	Unit	Rate Rs	Total Value Rs	Deduct Previous Measurement			Unit	Since last measurement		Remarks
							MB	Page	Quantity		Quantity	Value Rs	
1	Earth work excavation in all classes of soil(except hard rock which requires blasting) for foundation etc. including shoring shuttering and form work, removing the excavated earth to a safe place and back filling the same on the basement and compacting to correct profiles and foundation level including consolidation of useful earth for filling by ramming in 15 cm layers including all leads and lifts Qty wide page 3 MB		342.65	m3	80	27412				m3	342.65	27412	
2	providing and laying cement concrete 1:5:10 using 40 mm (nominal size) broken stone including edge shuttering form work watering, etc less cost of cement Qty wide page 3 MB		23.408	m3	1000	23408				m3	23.408	23408	

Account

Dr. SUNNY JOSEPH KALAYATHANKAL
M.Tech, MCA, M.Sc, M.Phil, B.Ed
Ph.D (Computer Science), Ph.D (Maths)
PRINCIPAL
Jyothi Engineering College
Cheruthuruthy P.O.- 679 531

3	Reinforced cement concrete 1 1/2 3 using 20mm nominal size broken stone for column, wall slab etc. including all form work watering curing etc complete but excluding cost of cement and reinforcement										
a	column- Qty wide page 7 MB	9.078	m3	2710	24601.38			m3	9.078	24601.38	
b	floor slab Qty wide page 5 MB	32.992	m3	2078	68557.37			m3	32.992	68557.37	
c	Roof slab Qty wide page 7 MB	27.572	m3	2258	62257.57			m3	27.572	62257.57	
d	wall Qty wide page 5 MB	28.516	m3	2710	77278.36			m3	28.516	77278.36	
4	Reinforcement for RCC Work bent, tied and placed in position using 18 gauge winding wire etc complete Qty wide page 6 MB 50	167.6	Qtl	300	50280			Qtl	167.6	50280	
5	Floor finish plastering with CM 1:3, 15mm thick two coats including a cement flushing coat for inner face of wall and floor of the tank watering curing etc complete but excluding cost of cement Qty wide page 11 MB	211.662	m2	60	12699.72			m2	211.662	12699.72	

Aman
 Dr. SUNNY JOSEPH KALAYATHANKAL
 M.Tech, MCA, M.Sc, M.Phil, B.Ed
 Ph.D (Computer Science), Ph.D (Maths)
 PRINCIPAL
 Jyothi Engineering College
 Cheruthuruthy P.O.- 679 531

6	plastering with cement with mortar 1:4, 12mm thick one coat outside of wall trowelled hard and finished smooth necessary cutting etc including watering curing etc complete but excluding cost of cement Qty wide page 11 MB	309.525	m2	50	15476.25				m2	309.525	15476.25
7	plastering under side of slab 1:3, 9mm thick one coat finished smooth with necessary cutting grooves including watering curing etc complete but excluding cost of cement Qty wide page 9 MB	218.71	m2	52	11372.92				m2	218.71	11372.92
8	plastering the top of cover slab with CM 1:3, 6mm thick one coat finished smooth including watering curing etc complete but excluding cost of cement Qty wide page 13 MB	229.445	m2	40	9177.8				m2	229.445	9177.8

Sunny
 Dr. SUNNY JOSEPH KALAYATHANKAL
 M.Tech, MCA, M.Sc, M.Phil, B.Ed
 Ph.D (Computer Science), Ph.D (Maths)
 PRINCIPAL
 Jyothi Engineering College
 Cheruthuruthy P.O.-679 531

9	Dadoing walls floor inside of tank with best quality glassed tiles (approved by site engineer) in CM 1 3, and pointing with white cement excluding cost of gray cement Qty wide page 15 MB	339.292	m2	260	88215.92				m2	339.292	88215.92
10	R R masonry in cement mortar 1.8, for foundation, basement, retaining wall etc. excluding cost of cement Not executed										
11	supplying and fixing cast iron cover slab of size 60*60cms manholes including providing locking arrangements Not executed										
	Extra item										
1	providing water cutting Qty wide page 13 MB	62.7	m	20	1254				m	62.7	1254
Total											471991.29

For United Construction Company

Managing Partner

Amud

Dr. SUNNY JOSEPH KALAYATHANKAL
M.Tech, MCA, M.Sc, M.Phil, B.Ed
Ph.D (Computer Science), Ph.D (Maths)
PRINCIPAL
Jyothi Engineering College
Cheruthuruthy P.O. - 679 531

EXPENDITURE DETAILS OF RAIN
WATER HARVESTING PROJECT

It is certified that an amount of **Rs.5382804** has been expended for rainwater harvesting project vide to following measurement books (MBs).

Sl no.	MB No.	Page No	Amount
a)	MB.83	19	1915091.00
b)	MB 60	28	904800.00
c)	MB 85	48	507200.00
d)	MB 84	78	1216163.00
e)	MB 83	106	839550.00
Total			5382804.00



[Handwritten signature in blue ink]

Jyothi Engineering College, Jyothi Hills, Vettikattiri, Cheruthuruthy, Thrissur 679 531

JEC/MMI/2013

STOCK REGISTER

(CENTRAL / DEPARTMENTAL / LABORATORY)

972

No.

Name of Dept: Store Name of Lab:

Name of Item: 160mm PVC pipe 6kg IST Unique No:

Sl. No.	Date	Purchase Order	Supplier / Issued to	Invoice No.	Rate	VAT	Total	Receipt / Issue	Balance	Initials	Remarks
1	24.6.16		Tube links Calicut	CLI-B/0676	45350	5%	5742.14 25623.31	126mts	126mts	X	11/2016
2	5-7-16		water Harvesting					108mts	18mts	X	
3	4-7-16		Water harvesting					6	12mts	X	
4	14-7-16		Return from work				13605.00	30mts	30mts	X	✓
5	16-5-20		New road work					12	18mts	X	
6	21-11-20		Road Crossing at New Campus					18mts	N/A	X	

Annex

DR. SUNNY JOSEPH KALAYATHAMKAL
 A. M. Sc, M. Phil, B. Ed
 Ph.D (Sci. Ed Science), Ph.D (M. Ed)
 PRINCIPAL
 Jyothi Engineering College
 Cheruthuruthy P.O.-679 531
